

Hardwick Project No. 1 – Hardwick Road Pumping System Upgrades

*Weekly Project Update (Issued on October 20, 2023)
Town of Hardwick, MA*



WORK PERFORMED DURING THE WEEK OF OCTOBER 16, 2023

- Contractor pumped out Eagle Hill Pump Station for bypass tie-in.
- Contractor shut down Eagle Hill Pump Station with Town.
- Contractor excavated sewer main on Route 32A and tied in new valves for the pump station.
- Contractor compacted and backfilled trench and prepped for paving.

KEY WORK ELEMENTS

- Pumped Out Eagle Hill Pump Station
- Excavated Sewer Main/Tied In Valves/Backfilled

CONTACT INFORMATION

Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com

WORK ANTICIPATED DURING THE WEEK OF OCTOBER 23, 2023


- Contractor plans to prep the site for dewatering area.
- Contractor plans to bring in trench shoring equipment.
- Contractor plans to begin excavating for Wetwell.
- Wetwell delivery is scheduled for week of 11/6.



Excavated Sewer Main



Placing Valves

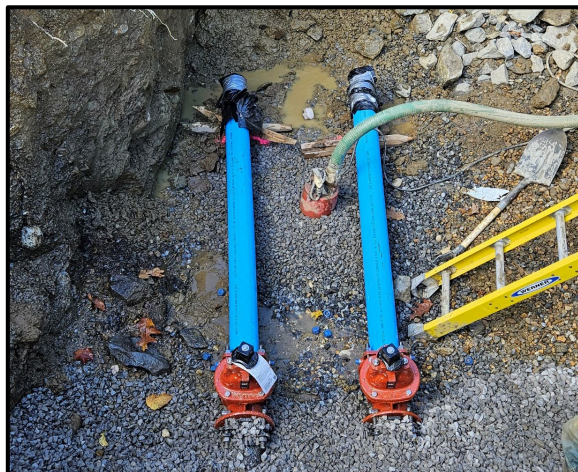

Tying In New Valves



Backfilled Trench
