

# Hardwick Project No. 1 – Hardwick Road Pumping System Upgrades

*Weekly Project Update (Issued on November 9, 2023)  
Town of Hardwick, MA*



## WORK PERFORMED DURING THE WEEK OF NOVEMBER 6, 2023

- Contractor continued preparing for the wetwell/valve vault delivery, including pumping water out of the wetwell/valve vault excavation.
- Wetwell/valve vault delivered and set on Wednesday 11/8.
- Contractor completed installation of the wetwell/valve vault.

## KEY WORK ELEMENTS

- Pumping Out Excavation for Wetwell/Valve Vault
- Installation of Wetwell/Valve Vault

## WORK ANTICIPATED DURING THE WEEK OF NOVEMBER 13, 2023

- Contractor plans to backfill and compact the wetwell/valve vault excavation.
- Contractor plans to begin excavation for building foundation.
- Contractor plans to begin installation of footings for building foundation.

## CONTACT INFORMATION

Justin Skelly, P.E.  
Senior Project Manager  
413-567-6310 (x703)  
[justin.skelly@dpcengineering.com](mailto:justin.skelly@dpcengineering.com)




*Pumped-Out Wetwell/Valve Vault  
Excavation*



*Silt Containment Area  
Excavation*



*Wetwell/Valve Vault Delivery*

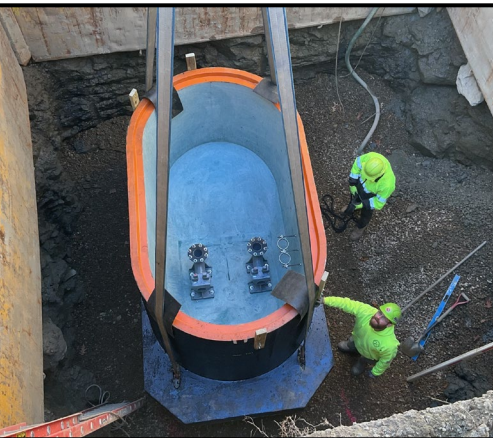

*Installation of Wetwell/Valve Vault*
