

## Project 2A – Wheelwright WPCF Upgrades Project

*Weekly Project Update (Issued on March 4, 2024)*  
**Town of Hardwick, MA**



### **WORK PERFORMED BY CONTRACTOR DURING THE WEEK OF FEBRUARY 26, 2024**

- Excavation for footings of new Effluent Building.
- Demolished existing/abandoned clarifier tank slab and existing manhole structure.
- Installed formwork for footings of new Effluent Building.
- Installed 8-inch ductile iron drain line for sump pump for new Effluent Building clearwell.

### **WORK ANTICIPATED BY CONTRACTOR DURING THE WEEK OF MARCH 4, 2024**


- Plans to continue installation of forms for footings for new Effluent Building.
- Plans to pour concrete for footings for new Effluent Building.

### **KEY WORK ELEMENTS**

- Demolition of Existing/Abandoned Clarifier Slab and Existing Sewage Pump Manhole
- Installation of Forms for Footings for New Effluent Filtration and UV Building.

### **CONTACT INFORMATION**

Justin Skelly, P.E.  
Senior Project Manager  
413-567-6310 (x703)  
[justin.skelly@dpcengineering.com](mailto:justin.skelly@dpcengineering.com)

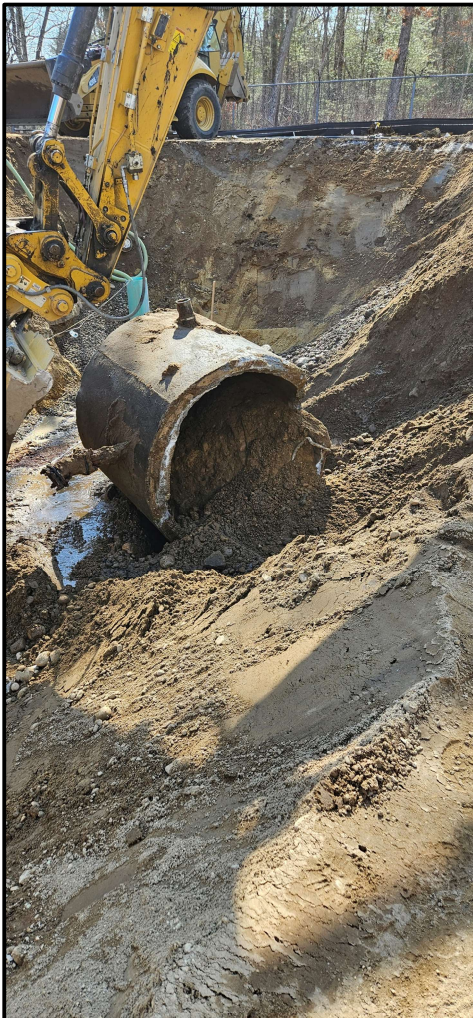

*Demolition of Existing Manhole*



*Installation of Forms for Footings*
